


M&I ENGINEERING SOLUTIONS

ID	Task Name	Resource Names	Duration	Start	Finish	Sun 3 May		Tue 5 May		Thu 7 May	
						0	0	0	0	0	0
1	MV "....." TOPSIDE TANK COATING PLAN m²		70 hrs	4 May 08:00	7 May 06:00						
2	No: PS Ballast Tank Coating Renewal with Chemco RS 500P & RA 500M - 1000 m²		62 hrs	4 May 08:00	6 May 22:00						
3	No:... PS Mud & Loose Scale Cleaning of Tank	Cleaner[4]	4 hrs	4 May 08:00	4 May 12:00						
4	No:... PS Staging	Cleaner[2]	2 hrs	4 May 12:00	4 May 14:00						
5	No:... PS Mechanical Surface Preperation	Mechanical Cl	4 hrs	4 May 14:00	4 May 18:00						
6	No:... PS Removal of Loose Scales and Coatings From The Surface With Waterjet(~750 bar)	Waterjet App.[2]	12 hrs	4 May 18:00	5 May 06:00						
7	No:... PS Removal of the Water From the Tank	Cleaner[3]	4 hrs	5 May 06:00	5 May 10:00						
8	No:... PS First Coat Paint Application (RS 500P Rust & Wet Tolerant 100% VS Class Approved Epoxy Coating)	Paint Applicator[4]	6 hrs	5 May 10:00	5 May 16:00						
9	No:... PS Stripe Coat (RA 500M - Wet tolerant - VS 100% Class Approved Glassflake Epoxy Coating)	Paint Applicator[4]	6 hrs	5 May 16:00	5 May 22:00						
10	No:... PS Final Coat (RA 500M - Glassflake Epoxy)	Paint Applicator[4]	8 hrs	5 May 22:00	6 May 06:00						
11	No:... PS Restaging and Tank Cleaning	Cleaner[4]	4 hrs	6 May 12:00	6 May 16:00						
12	No:... PS Ballasting of the Tank	Captain	2 hrs	6 May 20:00	6 May 22:00						
13	No: STBD Ballast Tank Coating Renewal with Chemco RS 500P & RA 500M - 1000 m²		66 hrs	4 May 12:00	7 May 06:00						
14	No:... STBD Mud & Loose Scale Cleaning of Tank	Cleaner[2]	8 hrs	4 May 12:00	4 May 20:00						
15	No:... STBD Staging	Cleaner[2]	2 hrs	4 May 20:00	4 May 22:00						
16	No:... STBD Mechanical Surface Preperation	Mechanical Cl	4 hrs	4 May 22:00	5 May 02:00						
17	No:... STBD Removal of Loose Scales and Coatings From The Surface With Waterjet (750 bar)	Waterjet App.[2]	12 hrs	5 May 02:00	5 May 14:00						
18	No:... STBD Removal of the Water from the tank	Cleaner[3]	4 hrs	5 May 14:00	5 May 18:00						
19	No:... STBD First Coat Paint Application (RS 500P Rust & Wet Tolerant 100% VS Class Approved Epoxy Coating)	Paint Applicator[4]	6 hrs	5 May 18:00	6 May 00:00						
20	No:... STBD Stripe Coat (RA 500M - Wet tolerant - VS 100% Class Approved Glassflake Epoxy Coating)	Paint Applicator[4]	6 hrs	6 May 00:00	6 May 06:00						
21	No:... STBD Final Coat (RA 500M - Glassflake Epoxy)	Paint Applicator[4]	8 hrs	6 May 06:00	6 May 14:00						
22	No:... STBD Restaging and Tank Cleaning	Cleaner[4]	4 hrs	6 May 20:00	7 May 00:00						
23	No:... STBD Ballasting of the Tank	Captain	2 hrs	7 May 04:00	7 May 06:00						

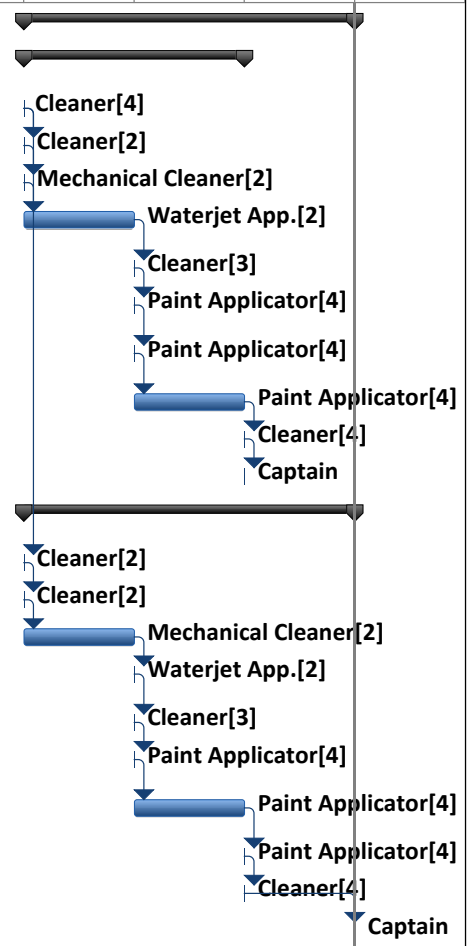

Project: MV "....."	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
