


Project: KARBALA RAFINERY PROJ Date: 22.12.14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Mode	Task Name	Duration	Start	Finish	Jan '15		Feb '15		Mar '15		Apr '15		May '15		Jun '15		Jul '15		Aug '15																
						14	21	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	12	19	26	03	10	17	24	31	07	14	21	28	05	12
23		Edge preparations	60 days	25.04.15	24.06.15																															
24		Bending Works	60 days	27.04.15	26.06.15																															
25		Stocking for transportation to vessel	60 days	04.05.15	03.07.15																															
26		<b>Third Group of Steel (8.000 Tonnes)</b>	<b>123 days</b>	<b>11.04.15</b>	<b>12.08.15</b>																															
27		Steel transportations to the Turkey	40 days	11.04.15	21.05.15																															
28		Steel plates transportations from port to shop primer facilities	5 days	21.05.15	26.05.15																															
29		Shop primer application of steel plates (~125Ton/day)	60 days	26.05.15	25.07.15																															
30		Stocking of the shop primed plates on workshop area	60 days	26.05.15	25.07.15																															
31		Cutting of new plates on CNC machine	60 days	29.05.15	28.07.15																															
32		Stocking of plates after CNC cutting	60 days	31.05.15	30.07.15																															
33		Transferring of steel plates to the yard area for edge preparation and bending works	60 days	02.06.15	01.08.15																															
34		Edge preparations	60 days	04.06.15	03.08.15																															
35		Bending Works	60 days	06.06.15	05.08.15																															
36		Stocking for transportation to vessel	60 days	13.06.15	12.08.15																															

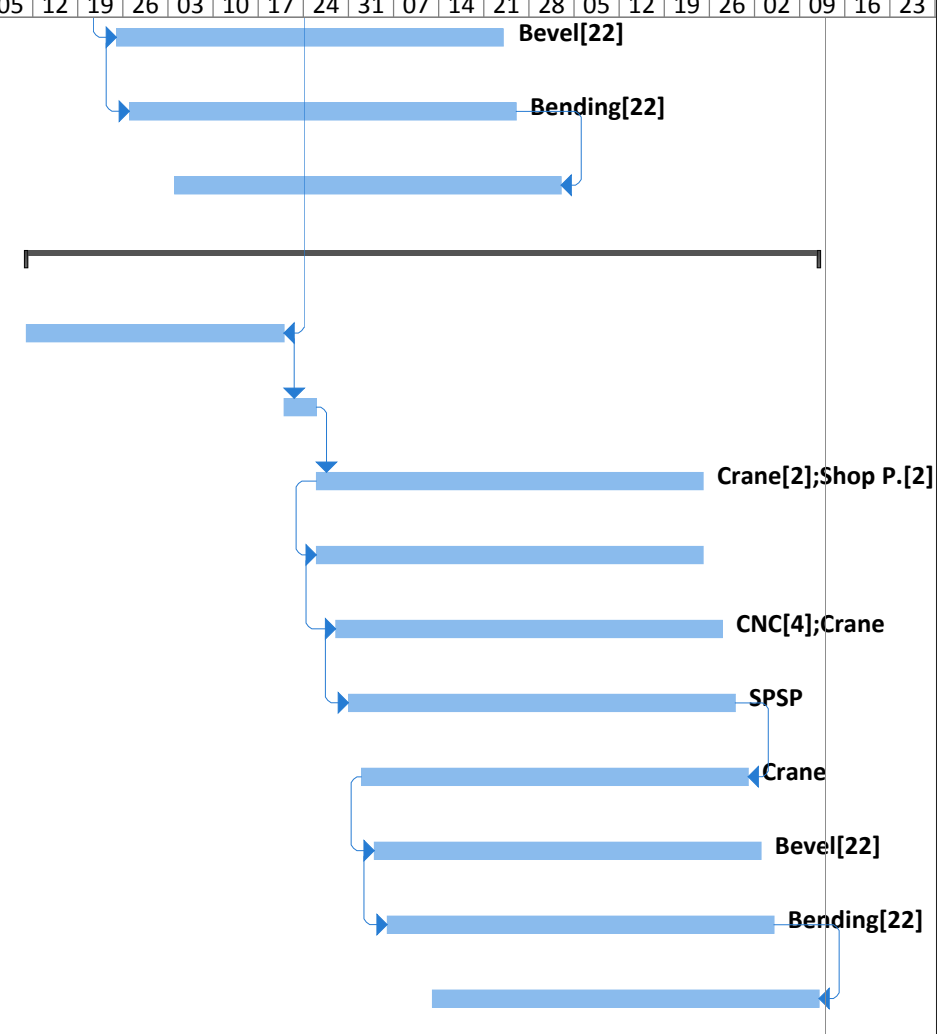

Project: KARBALA RAFINERY PROJ Date: 22.12.14	Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
	Split		External Tasks		Inactive Summary		Manual Summary		Progress	
	Milestone		External Milestone		Manual Task		Start-only		Manual Progress	
	Summary		Inactive Task		Duration-only		Finish-only			
